


Project: No.1 Magnetic Pad
Client: Gripple Ltd
Client's Order No: I4180
Inspection Date:
First: 20 / 04 / 2010

Certificate No: COV1019137
Office: Sheffield
Date: 20 / 04 / 2010
Order Status: Complete
Final: 14 / 07 / 2010

This certificate is issued to Gripple Ltd to certify that the undersigned surveyor did, at their request attend the premises at The Old West Gun Works, Sheffield on and between the above dates for the purpose of examining and witnessing tests on the items listed below. All tests produced satisfactory results.

TEST CONFIGURATION

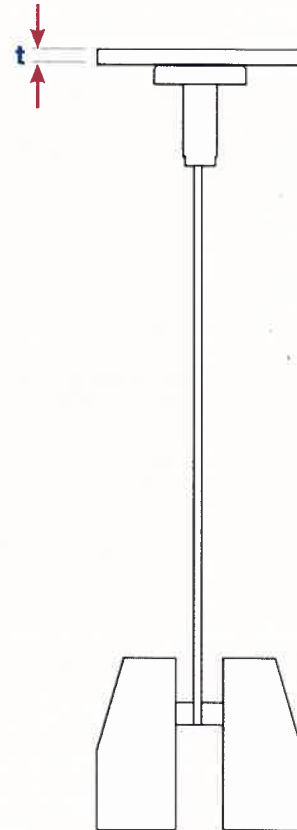

14/7/10

M Cobb
 Surveyor of Lloyd's Register

Gripple Model	Rope Construction	Gripple Rated Load	Gripple Load Limit 2:1	Metal Thickness (t)	Results *		
No.1 Magnetic Pad	7 x 7 (6/1)	0 - 3 kg / 0 - 6 lbs	6 kg / 12 lbs	1 mm	6 kg / 13 lbs	7 kg / 15 lbs	7 kg / 15 lbs
		0 - 6 kg / 0 - 13 lbs	12 kg / 26 lbs	2 mm	14 kg / 30 lbs	15 kg / 33 lbs	13 kg / 28 lbs
		0 - 8 kg / 0 - 17 lbs	16 kg / 34 lbs	3 mm	27 kg / 59 lbs	17 kg / 37 lbs	24 kg / 52 lbs

* The above test was conducted at a room temperature of 20°.
